

HARDWARE SCHEDULE SUBMITTAL

PROJECT: T2507 (second project)
DATE: 2026-10-10
PREPARED BY: Mobley Contracting

TABLE OF CONTENTS

1.	Cover Page	1
2.	Table of Contents	2
3.	Door Schedule (extracted) - 49 doors	3
4.	Source: 192a16af8f31ae0c.pdf (page 10 of 30)	5

Door Schedule (extracted)

T2507 (second project) - 49 doors read from 192a16af8f31ae0c.pdf

Machine-read from the uploaded schedule; values stay drafts until reviewed. (?) = not read with certainty, check it on the sheet. Source = page and table row on the uploaded sheet (appended at the end of this pack...

Mark	Hardware group	Size (W x H)	Thick.	Fire rating	Door type / matl / fin	Frame type / matl / fin	Notes	Source
100A	-	3'-0" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 100	p.10 row 0
101A	-	3'-0" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 101	p.10 row 1
102A	-	3'-0" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 102	p.10 row 2
103A	-	3'-0" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 103	p.10 row 3
104A	-	3'-0" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	3; Room: 104	p.10 row 4
105A	-	3'-0" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 105	p.10 row 5
106A	-	3'-0" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 106	p.10 row 6
107A	-	3'-0" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 107	p.10 row 7
108A	-	3'-0" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 108	p.10 row 8
109A	-	3'-0" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 109	p.10 row 9
110A	-	3'-0" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 110	p.10 row 10
113A	-	3'-0" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 113 S1	p.10 row 11
113B	-	3'-0" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 113 S1	p.10 row 12
114A	-	2'-8" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 114	p.10 row 13
115A	-	3'-0" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 115	p.10 row 14
115B	-	2'-8" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 115	p.10 row 15
116A	-	3'-0" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 116	p.10 row 16
116B	-	2'-8" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 116	p.10 row 17
117A	-	2'-8" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 117	p.10 row 18
118A	-	2'-8" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 118	p.10 row 19
119A	-	3'-0" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 119	p.10 row 20
120A	-	3'-0" x 7'-0"	-	-	D1 / HM / -	F1 / HM / -	2; Room: 120	p.10 row 21
121A	-	3'-0" x 7'-0"	-	-	D1 / HM / -	F1 / HM / -	2; Room: 121	p.10 row 22
122A	-	3'-0" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 122	p.10 row 23
123A	-	3'-0" x 7'-0"	-	-	D1 / HM / -	F1 / HM / -	2; Room: 123	p.10 row 24
124A	-	2'-8" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 124	p.10 row 25
125A	-	2'-8" x 7'-0"	-	-	D1 / HM / -	F1 / HM / -	2; Room: 125	p.10 row 26
126A	-	3'-0" x 7'-0"	-	-	D1 / HM / -	F1 / HM / -	2; Room: 126	p.10 row 27
127A	-	3'-0" x 7'-0"	-	-	D1 / HM / -	F1 / HM / -	2; Room: 127	p.10 row 28
128A	-	3'-0" x 7'-0"	-	-	D1 / HM / -	F1 / HM / -	2; Room: 128	p.10 row 29
128B	-	3'-0" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 128	p.10 row 30
129A	-	3'-8" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 129	p.10 row 31
129B	-	3'-8" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 129	p.10 row 32
130A	-	3'-0" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 130	p.10 row 33
131A	-	3'-0" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 131	p.10 row 34

Door Schedule (extracted) (continued)

T2507 (second project) - 49 doors read from 192a16af8f31ae0c.pdf

Machine-read from the uploaded schedule; values stay drafts until reviewed. (?) = not read with certainty, check it on the sheet. Source = page and table row on the uploaded sheet (appended at the end of this pack...

Mark	Hardware group	Size (W x H)	Thick.	Fire rating	Door type / matl / fin	Frame type / matl / fin	Notes	Source
131B	-	3'-0" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 131	p.10 row 35
132A	-	5'-6" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 132; Duplicate mark 1...	p.10 row 36
132A [ro...	-	6'-3" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 132; Duplicate mark 1...	p.10 row 37
132B	-	5'-6" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 132	p.10 row 38
133A	-	3'-0" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 133	p.10 row 39
136A	-	3'-0" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 136	p.10 row 40
137A	-	5'-0" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 137	p.10 row 41
138A	-	3'-0" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 138	p.10 row 42
139A	-	3'-0" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 139	p.10 row 43
140A	-	3'-0" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 140	p.10 row 44
141A	-	3'-0" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 141	p.10 row 45
141B	-	3'-0" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 141	p.10 row 46
142A	-	3'-0" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 142	p.10 row 47
143A	-	3'-0" x 7'-0"	-	-	EXIST / HM / -	EXIST / HM / -	1; Room: 143	p.10 row 48

ALL INTERIOR DOORS TO BE PAINTED AND NEW
HARDWARE INSTALLED. SAVE EXISTING LOCKSET,
HINGES AND WORKING CLOSERS TO BE REINSTALLED.

FINISH SCHEDULE							
ROOM #	ROOM NAME	BASE	NORTH	EAST	SOUTH	WEST	NOTES/REMARKS
100	CAN WASH	-	WF4	WF4	WF4	WF4	
101	SCULLERY	B3	WF1	WF1	WF1	WF1	1
102	FOOD PREP	B3	WF1	WF1	WF1	WF1	1
103	FOOD STORAGE	B3	WF1	WF1	WF1	WF1	1
104	CORRIDOR	B2	WF1	WF1	WF1	WF1	
105	MAINT / STOR	-	WF4	WF4	WF4	WF4	
106	MOTHERS CNTR	B1	WF1	WF1	WF1	WF1	
107	MAINT. EQUIP.	-	WF4	WF4	WF4	WF4	
108	OFFICE	B1	WF1	WF1	WF1	WF2	
109	BDE OP SGM	B1	WF1	WF1	WF1	WF2	
110	OP S-3	B1	WF1	WF1	WF1	WF2	
111	VEST.	B1	WF4	WF4	WF4	WF4	
112	LOBBY	B1(DRYWALL ONLY) B2	WF1	WF1	WF1	WF1	
113	S1 PERSONNEL SERVICES	B1	WF1	WF2	WF1	WF1	
114	BDE S1 OFFICER	B1	WF1	WF2	WF1	WF1	
115	BDE HR TECH	B1	WF1	WF2	WF1	WF1	
116	CLASSROOM	B1	WF1	WF1	WF1	WF2	
117	BDE CMD SGT MAJ	B1	WF1	WF1	WF1	WF1	
118	COMMANDER	B1	WF1	WF1	WF1	WF1	
119	AO/XO	B1	WF1	WF1	WF1	WF1	
120	SIPR ROOM	B1	WF1	WF1	WF1	WF1	
121	MECH	-	WF1	WF1	WF1	WF1	
122	STO.	-	WF1	WF1	WF1	WF1	
123	S-4	B1	WF2	WF1	WF1	WF1	
124	OFFICE	B1	WF2	WF1	WF1	WF1	
125	OFFICE	B1	WF2	WF1	WF1	WF1	
126	WOMENS	B3	SEE FINISH PLAN	SEE FINISH PLAN	SEE FINISH PLAN	SEE FINISH PLAN	
127	MENS	B3	SEE FINISH PLAN	SEE FINISH PLAN	SEE FINISH PLAN	SEE FINISH PLAN	
128	MECH	-	WF1	WF1	WF1	WF1	
129	UNIT ADMIN	B1	WF1	WF1	WF1	WF1	
130	STO	B1	WF1	WF1	WF1	WF1	
131	EXCERCISE ROOM	B1	WF1	WF1	WF1	WF1	
132	DRILL FLOOR	B1 (DRYWALL ONLY) B2	WF1	WF1	WF1	WF1	EXISTING MURAL AND GREEN WALL TO REMAIN. PAINT WF1 ABOVE
133	SUPPLY OFFICE	B1	WF1	WF1	WF1	WF1	
134	ARMS VAULT	EXT	EXT	EXT	EXT	EXT	
135	UNIT STORAGE	-	WF1	WF1	WF1	WF1	
136	RECRUITER	B1	WF2	WF1	WF1	WF1	
137	STORAGE	B1	WF1	WF1	WF1	WF1	
138	MECHMAIL ROOM	-	WF1	WF1	WF1	WF1	
139	CHAPLAINS OFFICE	B1	WF1	WF1	WF1	WF1	
140	TACTICAL OP. CNTR	B1	WF1	WF1	WF1	WF1	
141	HHO CMND TEAM	B1	WF2	WF1	WF1	WF1	
142	LEGAL	B1	WF1	WF1	WF1	WF1	
143	TROOP CMDR	B1	WF2	WF1	WF1	WF1	

DOOR SCHEDULE										
ROOM	NAME	MARK	DOOR				FRAME		SET NO.	NOTES
			SIZE		MATL	TYPE	MATL	TYPE		
			WD	HGT						
100	CAN WASH	A	3'-0"	7'-0"	HM	EXIST	HM	EXIST		1
101	SCULLERY	A	3'-0"	7'-0"	HM	EXIST	HM	EXIST		1
102	FOOD PREP	A	3'-0"	7'-0"	HM	EXIST	HM	EXIST		1
103	FOOD STORAGE	A	3'-0"	7'-0"	HM	EXIST	HM	EXIST		1
104	CORRIDOR	A	3'-0"	7'-0"	HM	EXIST	HM	EXIST		3
105	MAINT / STOR	A	3'-0"	7'-0"	HM	EXIST	HM	EXIST		1
106	MOTHERS CNTR	A	3'-0"	7'-0"	HM	EXIST	HM	EXIST		1
107	MAINT. EQUIP.	A	3'-0"	7'-0"	HM	EXIST	HM	EXIST		1
108	OFFICE	A	3'-0"	7'-0"	HM	EXIST	HM	EXIST		1
109	BDE OP SGM	A	3'-0"	7'-0"	HM	EXIST	HM	EXIST		1
110	OP S-3	A	3'-0"	7'-0"	HM	EXIST	HM	EXIST		1
113	S1 PERSONNEL SERVICES	A	3'-0"	7'-0"	HM	EXIST	HM	EXIST		1
113	S1 PERSONNEL SERVICES	B	3'-0"	7'-0"	HM	EXIST	HM	EXIST		1
114	BDE S1 OFFICER	A	2'-8"	7'-0"	HM	EXIST	HM	EXIST		1
115	BDE HR TECH	A	3'-0"	7'-0"	HM	EXIST	HM	EXIST		1
115	BDE HR TECH	B	2'-8"	7'-0"	HM	EXIST	HM	EXIST		1
116	CLASSROOM	A	3'-0"	7'-0"	HM	EXIST	HM	EXIST		1
116	CLASSROOM	B	2'-8"	7'-0"	HM	EXIST	HM	EXIST		1
117	BDE CMD SGT MAJ	A	2'-8"	7'-0"	HM	EXIST	HM	EXIST		1
118	COMMANDER	A	2'-8"	7'-0"	HM	EXIST	HM	EXIST		1
119	AO/XO	A	3'-0"	7'-0"	HM	EXIST	HM	EXIST		1
120	SIPR ROOM	A	3'-0"	7'-0"	HM	D1	HM	F1		2
121	MECH	A	3'-0"	7'-0"	HM	D1	HM	F1		2
122	STO.	A	3'-0"	7'-0"	HM	EXIST	HM	EXIST		1
123	S-4	A	3'-0"	7'-0"	HM	D1	HM	F1		2
124	OFFICE	A	2'-8"	7'-0"	HM	EXIST	HM	EXIST		1
125	OFFICE	A	2'-8"	7'-0"	HM	D1	HM	F1		2
126	WOMENS	A	3'-0"	7'-0"	HM	D1	HM	F1		2
127	MENS	A	3'-0"	7'-0"	HM	D1	HM	F1		2
128	MECH	A	3'-0"	7'-0"	HM	D1	HM	F1		2
128	MECH	B	3'-0"	7'-0"	HM	EXIST	HM	EXIST		1
129	UNIT ADMIN	A	3'-8"	7'-0"	HM	EXIST	HM	EXIST		1
129	UNIT ADMIN	B	3'-8"	7'-0"	HM	EXIST	HM	EXIST		1
130	STO	A	3'-0"	7'-0"	HM	EXIST	HM	EXIST		1
131	EXCERCISE ROOM	A	3'-0"	7'-0"	HM	EXIST	HM	EXIST		1
131	EXCERCISE ROOM	B	3'-0"	7'-0"	HM	EXIST	HM	EXIST		1
132	DRILL FLOOR	A	5'-6"	7'-0"	HM	EXIST	HM	EXIST		1
132	DRILL FLOOR	A	6'-3"	7'-0"	HM	EXIST	HM	EXIST		1
132	DRILL FLOOR	B	5'-6"	7'-0"	HM	EXIST	HM	EXIST		1
133	SUPPLY OFFICE	A	3'-0"	7'-0"	HM	EXIST	HM	EXIST		1
136	RECRUITER	A	3'-0"	7'-0"	HM	EXIST	HM	EXIST		1
137	STORAGE	A	5'-0"	7'-0"	HM	EXIST	HM	EXIST		1
138	MECHMAIL ROOM	A	3'-0"	7'-0"	HM	EXIST	HM	EXIST		1
139	CHAPLAINS OFFICE	A	3'-0"	7'-0"	HM	EXIST	HM	EXIST		1
140	TACTICAL OP. CNTR	A	3'-0"	7'-0"	HM	EXIST	HM	EXIST		1
141	HHID CMND TEAM	A	3'-0"	7'-0"	HM	EXIST	HM	EXIST		1
141	HHID CMND TEAM	B	3'-0"	7'-0"	HM	EXIST	HM	EXIST		1
142	LEGAL	A	3'-0"	7'-0"	HM	EXIST	HM	EXIST		1
143	TROOP CMDR	A	3'-0"	7'-0"	HM	EXIST	HM	EXIST		1

GENERAL DOOR NOTES:
(NOTES APPLY TO DOOR SCHEDULE ONLY)

- LOCATE TRANSITION STRIPS (IF REQUIRED) CENTERED BENEATH DOOR LEAF.
- PROVIDE PREFINISHED PAN/SILL AND DRIP EDGE FLASHING AT ALL EXTERIOR LOCATIONS PER MANUFACTURERS RECOMMENDATIONS.
- PROVIDE HEADERS AND LINTELS ABOVE ALL NEW OPENINGS. ALL DOORS SHALL BE 1 3/4" THICK, U.N.O.
- PRIME AND PAINT ALL HOLLOW METAL DOORS AND FRAMES. ARCHITECT TO SELECT COLOR FROM FULL RANGE OF COLORS. FRAMES IN ACCENT WALLS SHALL MATCH ACCENT COLORS.
- COORDINATE HARDWARE REQUIREMENTS WITH SECURITY VENDOR TO PROVIDE FULLY FUNCTIONAL INTEGRATED SYSTEM. ALL HOLLOW METAL FRAMES SHALL HAVE A 2" JAMB, 4" HEADS, X 5 3/4" FACE DIMENSION, U.N.O.

DOOR AND FRAME KEY:



NEW HOLLOW METAL DOOR - INTERIOR UNINSULATED DOOR (SINGLE) PER DOOR SCHEDULE - PAINT.



NEW HOLLOW METAL FRAME - 5 3/4" FULLY WELDED, FULLY GROUTED FRAME PER DOOR SCHEDULE - PAINT. FRAME FACE TO BE 2" JAMB AND 4" HEADS - TYP. SEE SPECS.

DOOR SCHEDULE NOTES / REMARKS:

(NOTES APPLY TO DOOR SCHEDULE ONLY)

- EXISTING DOOR TO REMAIN - PAINT. INSTALL NEW HARDWARE SET, USE EXISTING CORES & HINGES.
- NEW OPENING. PROVIDE NEW DOOR, FRAME AND HARDWARE.
- PROVIDE NEW HARDWARE TO MAKE DOOR CLOSE PROPERLY.

NOTATION LEGEND:

T TEMPERED SAFETY GLASS
H.M. HOLLOW METAL
ALUM. ALUMINUM
PF PRE-FINISHED (MANUFACTURER) SURFACE
PT PAINTED SURFACE (IN FIELD)

FINISH SCHEDULE NOTES / REMARKS:

(NOTES APPLY TO FINISH SCHEDULE ONLY)

- REPAIR THE GROUT JOINTS IN THE EXISTING WALL AS REQUIRED FOR PAINT.

FLOOR FINISH TYPES:

FF1: LVT TILE, SEE SPECIFICATIONS.
FF2A: EPOXY (TYPE 1) SEE SPECIFICATIONS.
FF2B: EPOXY (TYPE 2) SEE SPECIFICATIONS.
FF3: EXISTING CONCRETE FLOOR REMAINS
FF4: PROVIDE CONCRETE INFILL AT DEMOED FLOR AREA, MATCH EXISTING.

BASE TYPES:

B1: 4" VINYL BASE, COLOR BY ARCHITECT.
B2: PREP AND PAINT EXISTING GLAZED BLOCK AT BASE TO MATCH WALL COLOR, PAINT SYSTEM CMU-2
B3: INTEGRAL EPOXY BASE TO MATCH FLOORING.

WALL FINISH TYPES:

WF1: PAINT - FIELD COLOR, COLOR BY ARCHITECT, SEE SPECIFICATIONS.
WF2: PAINT - ACCENT COLOR, COLOR BY ARCHITECT, SEE SPECIFICATIONS.
WF4: EXISTING FINISH TO REMAIN. PATCH AND REPAIR WALL IF DAMAGED.
CMU-E1: EPOXY, SEE SPECS
CMU-E2: EPOXY, SEE SPECS
CMU-E3: EPOXY, SEE SPECS
FG-R1: EPOXY, SEE SPECS


FLOOR FINISH LEGEND

FF1: LVT TILE.

FF2A: EPOXY (TYPE 1)

FF2B: EPOXY (TYPE 2)

FF3: PROVIDE CONCRETE INFILL AT DEMOED FLOOR AREA, MATCH EXISTING.
EXISTING CONCRETE FLOOR OR FINISH TO REMAIN.

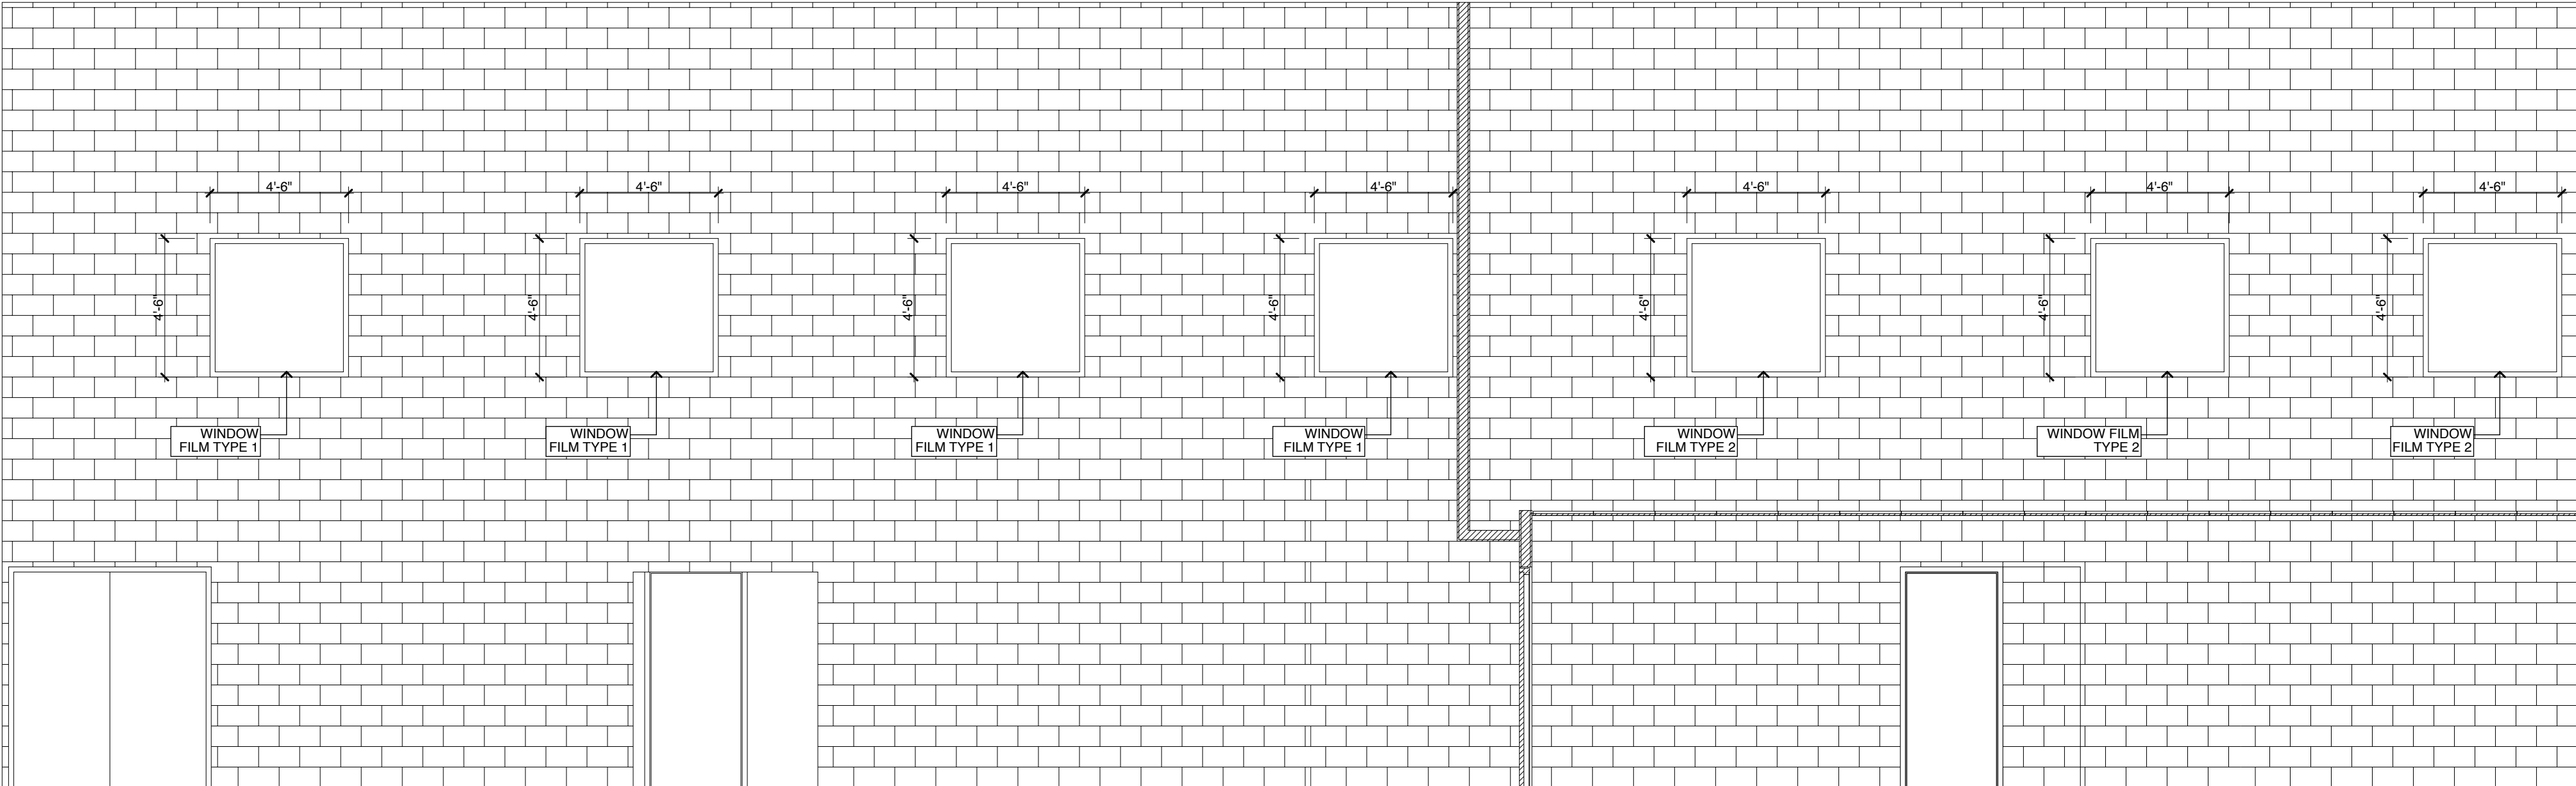

10 FRAME ELEVATION
SCALE: 1/4" = 1'-0"

STATE OF MISSOURI

MIKE KEHOE,

GOVERNOR



DAKE I WELLS
architecture

134 Park Central Square, Suite 300
St. Louis, MO 63103
P: 633.518.4545

Copyright 2025, Dake Wells Architecture, Inc. - Missouri State Certificate of Authority #0095589

OFFICE OF
ADMINISTRATION
DIVISION OF FACILITIES
MANAGEMENT,
DESIGN AND
CONSTRUCTION
DEPARTMENT OF
MISSOURI NATIONAL
GUARD

LEBANON READINESS
CENTER - REPAIRS TO
INTERIOR / EXTERIOR

301 WEST FREMONT
LEBANON, MISSOURI,
65536

PROJECT # T2507-01

SITE # 6286

FACILITY # 8136286002

REVISION:
DATE:
REVISION:
DATE:
REVISION:
DATE:
ISSUE DATE: 11/07/2025

CAD DWG FILE:T2507-01

DRAWN BY: EW

CHECKED BY: CS

DESIGNED BY: EW/CS

SHEET TITLE:
SCHEDULES
AND FRAME
TYPES

SHEET NUMBER:

A-103

10 OF 30 SHEETS

11/07/25
